

KIRBY INLAND MARINE

ANNUAL CARGO PIPING AND HOSE TEST REPORT SUMMERY

Reference: 33CFR 156.170

A copy of this report is to be retained on board the vessel.

VESSEL NAME: 407

DATES TESTS PERFORMED: PIPING 11 May 17

SIX INCH HOSE 14 FEB 17
FOUR INCH HOSE 17 NOV 17
SIX INCH HOSE 15 SEPT 17

PRESSURE RELIEF VALVE 11 MAY 17
GAUGES 11 May 17/ AIR RECEIVER RELIEF VALVE 11 MAY 17
FIXED PIPING: TESTED 11 MAY 17, MAWP: 125 PSI TEST PSI: 200 PSI
(At least 1.5 times maximum allowable working pressure(MAWP). MAWP is the relief valve setting.)

PRESSURE RELIEF VALVES: TESTED @ 125 P.S.I. ON 11 MAY 17
TRANSFER SYSTEM GAUGES WITHIN 10%: TESTED 11 MAY 17

HOSE 6"X60' SER #53976-3: TESTED 14 FEB 17, MAWP: 125 PSI TEST PSI: 200 PSI,

HOSE 6"X75' SER #52874-2: TESTED 15 SEPT 17, MAWP: 125 PSI TEST PSI: 200 PSI,


HOSE 4"X75' SER #53976-5: TESTED 17 NOV 17, MAWP: 125 PSI TEST PSI: 200 PSI,

Test performed at: MIAMI, FL.
Test method: HYDRO TEST

Signature:

Name:

Title:

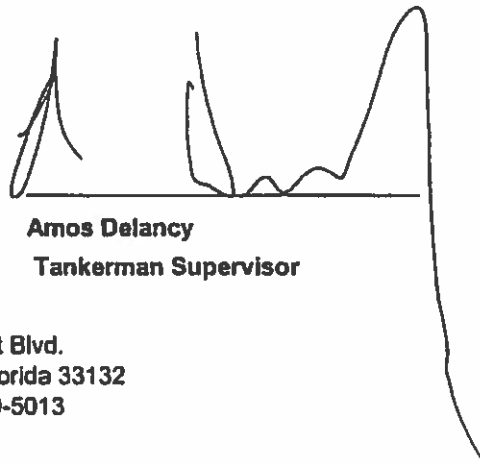

Amos Delancy
Tankerman Supervisor

Company address: 1020 Port Blvd.
Miami, Florida 33132
Telephone: (305) 579-5013
