

KIRBY INLAND MARINE

ANNUAL CARGO PIPING AND HOSE TEST REPORT

Reference: 33CFR 156.170

A copy of this report is to be retained on board the vessel.

Vessel Name:401

DATES TEST PERFORMED : PIPING 10 MAY 2021
CARGO PRESSURE RELIEF VALVES 10 MAY 2021
CARGO PRESSURE GAUGES 10 MAY 2021
AIR RECEIVER 10 MAY 21

PORTABLE HOSE # 1: TESTED 10 MAY 21, MAWP: 125 PSI TEST PSI 200
4" x 75 WILCOX #1151 GG MARINE MASTER DOCK HOSE SER. # 82083-3

PORTABLE HOSE # 3: TESTED 10 MAY 21, MAWP :125 PSI TEST PSI 200
6" x 75 WILCOX #1151 GG MARINE MASTER DOCK HOSE SER. # 70930


PORTABLE HOSE # 4: TESTED 10 MAY 21, MAWP :125 PSI TEST PSI 200
6" x 75 WILCOX #1151 GG MARINE MASTER DOCK HOSE SER. # 82083-2

PORTABLE HOSE # 5: TESTED 10 MAY 21, MAWP: 125 PSI TEST PSI 200
6" x 75 WILCOX #1151 GG MARINE MASTER DOCK HOSE SER. # 70906-1

Test performed at: **Port of Miami, Florida**

Test method: **Hydro Test**

Signature:

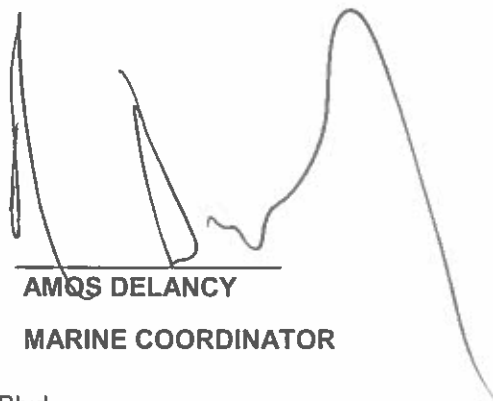

AMOS DELANCY

Title:

MARINE COORDINATOR

Company addr

1020 Port Blvd.
Miami, Florida 33132

Telephone:

(305)579-5013
